



APM Buildings Quotation Package



QUOTATION FOR:
Ag Building Ag304010

CONTACT:
1-888-261-2488

CONSTRUCTION: Post Frame
DIMENSIONS: 30' X 40' X 10'

SPECIFICATIONS FOR 30' X 40' X 10' POST FRAME PACKAGE:

● **MATERIAL PACKAGE**

- Pre-Engineered Wood Trusses (4/12 Pitch, 4' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Eave Posts (8' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Gable Posts (10' O/C)
- 2 x 8 Treated Skirt Boards (1 Row)
- 2 x 4 Wall Girts (24" O/C) and Roof Purlins (24" O/C)
- 2 x 10 Double Top Girt Truss Carrier
- Beige Tuff Rib 3 Panel Steel Siding
- Forest Green Tuff Rib 3 Panel Steel Roof
- No Concrete Provided

● **DOORS & WINDOWS**


- One 3' 6 Panel Entry Door
- Two 12' X 10' 2" Double Sliders
- One Stock Windows 3' x 3' 8" Single Hung Window

● **12" EAVE OVRHG., 0" GABLE OVRHG. W/ VENTED STEEL SOFFIT**

● **FASTENERS**

- 1 In.Metal to Wood Screws for Steel Wall, Roof Panels
- 4.5 Headlok Screws for Truss Carrier
- 16D Galv. Nails for Skirt Board
- Galvanized Steel Framing Nails

● **DETAILED BUILDING PLANS**

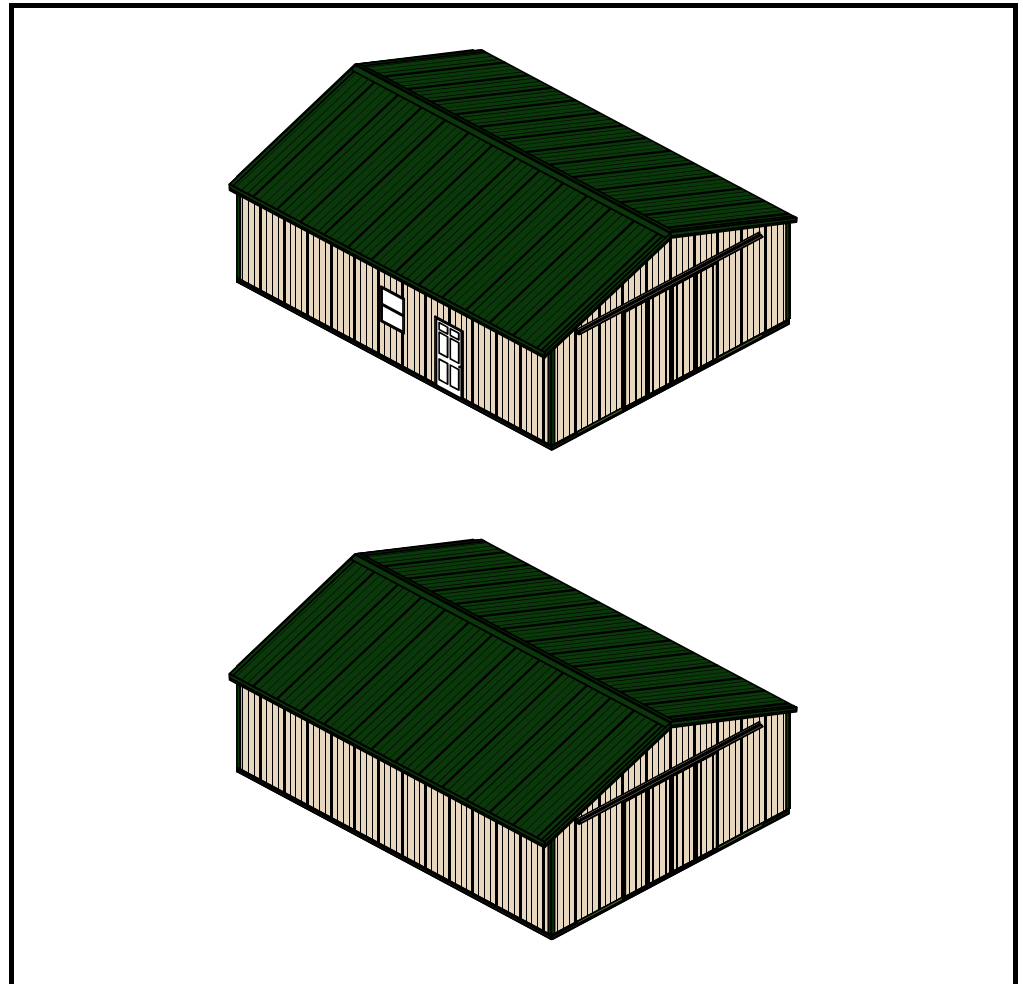

Subtotal	\$10,251.38
Discount	(\$1,435.00)
Total	\$8,816.38

ESTIMATE NUMBER: 19854



POLE LAYOUT
Personal Use, 1200 sq. ft.



Eave 1

