



APM Buildings Quotation Package



QUOTATION FOR:

Residential Res243210

CONTACT:

1-888-261-2488

CONSTRUCTION:

Post Frame

DIMENSIONS:

24' X 32' X 10'

SPECIFICATIONS FOR 24' X 32' X 10' POST FRAME PACKAGE:

• **MATERIAL PACKAGE**

- Pre-Engineered Wood Trusses (4/12 Pitch, 4' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Eave Posts (8' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Gable Posts (8' O/C)
- 2 x 8 Treated Skirt Boards (1 Row)
- 2 x 4 Wall Girts (24" O/C) and Roof Purlins (24" O/C)
- 2 x 10 Double Top Girt Truss Carrier
- Beige Tuff Rib 3 Panel Steel Siding
- Forest Green Tuff Rib 3 Panel Steel Roof
- No Concrete Provided

• **DOORS & WINDOWS**


- Two 9 X 8 Clopay T52S Ins. Std. Trk. w/o Openers
- One 3' 6 Panel Entry Door
- One Stock Windows 3' x 3' 8" Single Hung Window

• **12" EAVE OVRHG., 0" GABLE OVRHG. W/ VENTED STEEL SOFFIT**

• **FASTENERS**

- 1 In.Metal to Wood Screws for Steel Wall, Roof Panels
- 4.5 Headlok Screws for Truss Carrier
- 16D Galv. Nails for Skirt Board
- Galvanized Steel Framing Nails

• **DETAILED BUILDING PLANS**

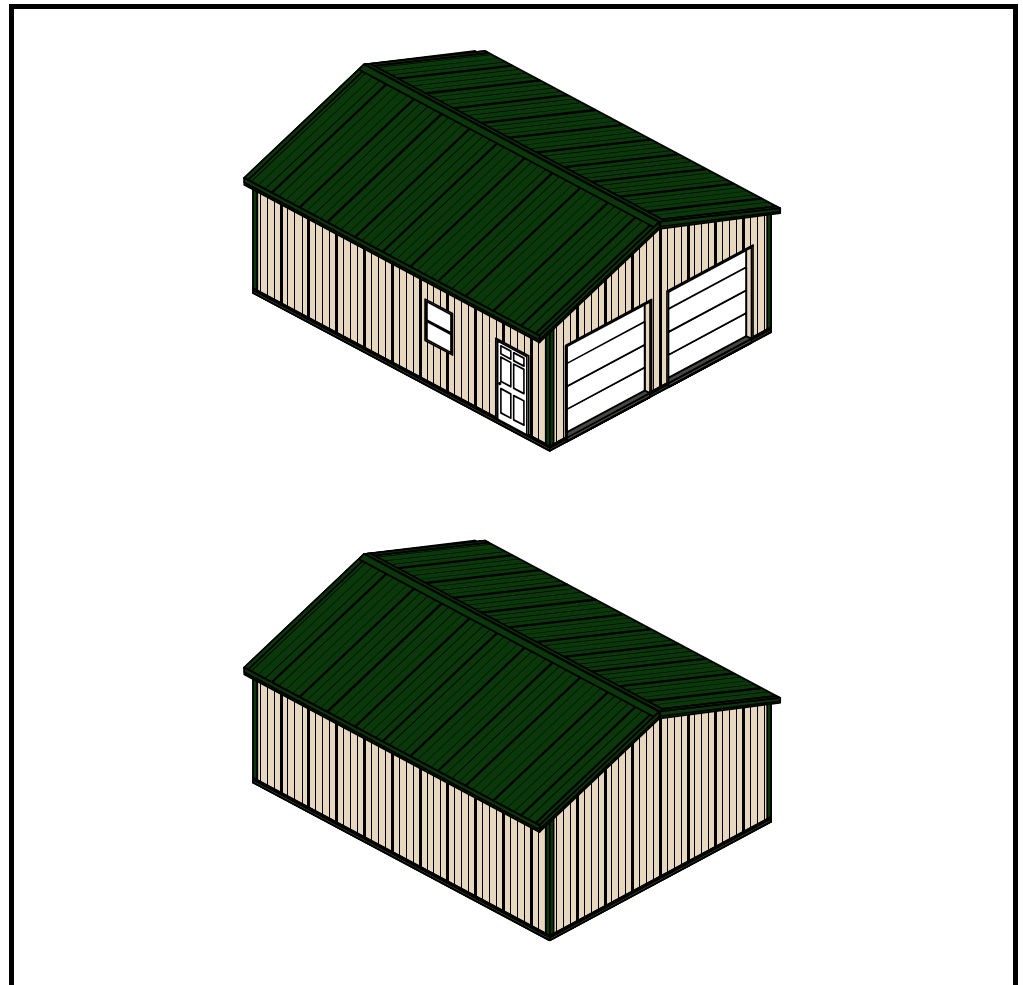

| | |
|--------------|-------------------|
| Subtotal | \$7,831.05 |
| Discount | (\$939.00) |
| Total | \$6,892.05 |

ESTIMATE NUMBER: 19838

Eave 1

