

**QUOTATION FOR:**

Horse Barn Horse363612

**CONTACT:**

1-888-261-2488

**CONSTRUCTION:**

Post Frame

**DIMENSIONS:**

36' X 36' X 12'

**EAVE1 PORCH**

10' X 36' X 9' 3"

**EAVE2 PORCH**

10' X 36' X 9' 3"

**SPECIFICATIONS FOR 36' X 36' X 12' POST FRAME PACKAGE:**

• **MATERIAL PACKAGE**

- Pre-Engineered Wood Trusses (4/12 Pitch, 4' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Eave Posts (8' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Gable Posts (8' O/C)
- 2 x 8 Treated Skirt Boards (1 Row)
- 2 x 4 Wall Girts (24" O/C) and Roof Purlins (24" O/C)
- 2 x 12 Double Top Girt Truss Carrier
- Beige Tuff Rib 3 Panel Steel Siding
- Forest Green Tuff Rib 3 Panel Steel Roof
- No Concrete Provided

• **DOORS & WINDOWS**

- Six 4' X 7' General Openings
- One 3' 6 Panel Entry Door
- Two 12' X 12' 2" Double Sliders
- One Stock Windows 3' x 3' 8" Single Hung Window


• **10' X 9' 3" X 36' DUAL PITCH PORCH ON BOTH EAVES**

• **12" EAVE OVRHG., 0" GABLE OVRHG. W/ VENTED STEEL SOFFIT**

• **FASTENERS**

- 1 In.Metal to Wood Screws for Steel Wall, Roof Panels
- 4.5 Headlok Screws for Truss Carrier
- 16D Galv. Nails for Skirt Board
- Galvanized Steel Framing Nails

• **DETAILED BUILDING PLANS**

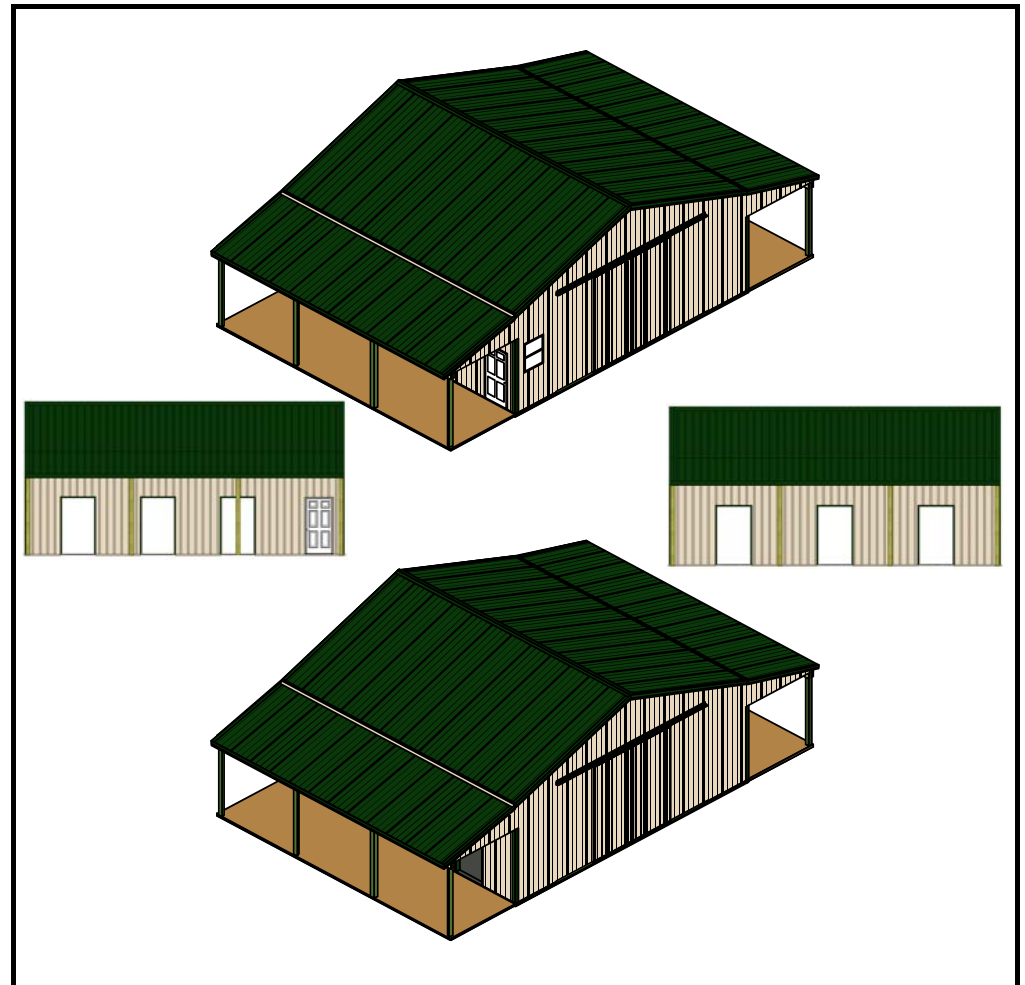

Subtotal	\$15,447.81
Discount	(\$2,162.00)
<b>Total</b>	<b>\$13,285.81</b>

ESTIMATE NUMBER: 19891



**POLE LAYOUT**  
Personal Use, 1296 sq. ft.



**Eave 1**

