



APM Buildings Quotation Package



QUOTATION FOR:

Horse Barn Horse364812

CONTACT:

1-888-261-2488

CONSTRUCTION:

Post Frame

DIMENSIONS:

36' X 48' X 12'

EAVE1 PORCH

10' X 48' X 9' 3"

EAVE2 PORCH

10' X 48' X 9' 3"

SPECIFICATIONS FOR 36' X 48' X 12' POST FRAME PACKAGE:

• **MATERIAL PACKAGE**

- Pre-Engineered Wood Trusses (4/12 Pitch, 4' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Eave Posts (8' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Gable Posts (8' O/C)
- 2 x 8 Treated Skirt Boards (1 Row)
- 2 x 4 Wall Girts (24" O/C) and Roof Purlins (24" O/C)
- 2 x 12 Double Top Girt Truss Carrier
- Beige Tuff Rib 3 Panel Steel Siding
- Forest Green Tuff Rib 3 Panel Steel Roof
- No Concrete Provided

• **DOORS & WINDOWS**

- Eight 4' X 7' General Openings
- One 3' 9 Lite Entry Door
- Two 12' X 12' 2" Double Sliders
- One Stock Windows 3' x 3' 8" Single Hung Window


• **10' X 9' 3" X 48' DUAL PITCH PORCH ON BOTH EAVES**

• **12" EAVE OVRHG., 0" GABLE OVRHG. W/ VENTED STEEL SOFFIT**

• **FASTENERS**

- 1 In.Metal to Wood Screws for Steel Wall, Roof Panels
- 4.5 Headlok Screws for Truss Carrier
- 16D Galv. Nails for Skirt Board
- Galvanized Steel Framing Nails

• **DETAILED BUILDING PLANS**

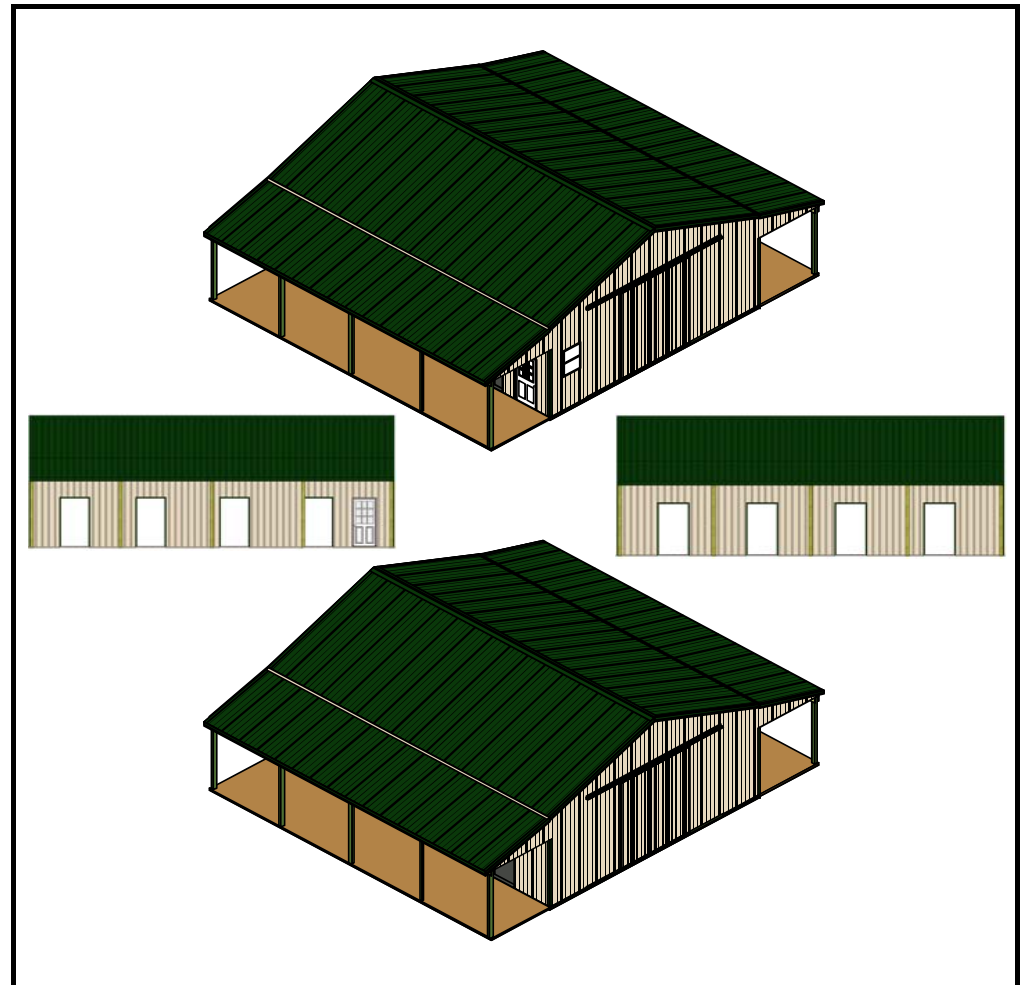

Subtotal	\$18,473.68
Discount	(\$2,586.00)
Total	\$15,887.68

ESTIMATE NUMBER: 19890



POLE LAYOUT
Personal Use, 1728 sq. ft.



Eave 1

